


		Nombre	Duracion	Inicio	Terminado	Predecesores
1		<b>FASE 1. ANALISIS DE FACTIBILIDAD</b>	<b>11.429 d...</b>	<b>9/05/18 08:00 AM</b>	<b>22/05/18 05:00 PM</b>	
2		Reunión con los interesados	3.429 days	9/05/18 08:00 AM	11/05/18 05:00 PM	
3		Análisis de solicitud de proyecto	5.714 days	14/05/18 08:00 AM	18/05/18 05:00 PM	2
4		Elaboración del project charter	2.286 days	21/05/18 08:00 AM	22/05/18 05:00 PM	3
5		<b>FASE 2. LEVANTAMIENTO DE REQU...</b>	<b>17.6 days</b>	<b>23/05/18 08:00 AM</b>	<b>13/06/18 11:12 AM</b>	
6		Sesiones de levantamiento	1.6 days	23/05/18 08:00 AM	24/05/18 11:12 AM	4
7		Análisis de procesos	1.143 days	24/05/18 11:12 AM	25/05/18 11:12 AM	6
8		Propuesta de solución	1.143 days	25/05/18 11:12 AM	28/05/18 11:12 AM	7
9		Priorización de requerimientos	1.143 days	28/05/18 11:12 AM	29/05/18 11:12 AM	8
10		Definición de alcance	2.286 days	29/05/18 11:12 AM	31/05/18 11:12 AM	9
11		Definición de herramientas de desar...	3.429 days	31/05/18 11:12 AM	5/06/18 11:12 AM	10
12		Confirmación de estándares de des...	3.429 days	5/06/18 11:12 AM	8/06/18 11:12 AM	11
13		Definición y solicitud de requerimien...	3.429 days	8/06/18 11:12 AM	13/06/18 11:12 AM	12
14		<b>FASE 3. DISEÑO DE LA SOLUCION</b>	<b>32 days</b>	<b>13/06/18 11:12 AM</b>	<b>23/07/18 11:12 AM</b>	
15		Diseño de interface de usuario (visu...	3.429 days	13/06/18 11:12 AM	18/06/18 11:12 AM	13
16		Diseño de modulos y objetos	5.714 days	18/06/18 11:12 AM	25/06/18 11:12 AM	15
17		Diseño de flujos y etapas	11.429 d...	25/06/18 11:12 AM	9/07/18 11:12 AM	16
18		Controles de sistemas (seguridad)	3.429 days	9/07/18 11:12 AM	12/07/18 11:12 AM	17
19		Diseño de base de datos	3.429 days	12/07/18 11:12 AM	17/07/18 11:12 AM	18
20		Diseño de casos de uso	3.429 days	17/07/18 11:12 AM	20/07/18 11:12 AM	19
21		Listado de tareas	1.143 days	20/07/18 11:12 AM	23/07/18 11:12 AM	20
22		<b>FASE 4. DESARROLLO DE LA SOLU...</b>	<b>66.286 d...</b>	<b>23/07/18 11:12 AM</b>	<b>11/10/18 11:12 AM</b>	
23		Codificación	45.714 d...	23/07/18 11:12 AM	17/09/18 11:12 AM	21
24		Documentación de código y objetos	5.714 days	17/09/18 11:12 AM	24/09/18 11:12 AM	23
25		Validación de casos de uso	3.429 days	24/09/18 11:12 AM	27/09/18 11:12 AM	24
26		Modelo de integración e implementa...	5.714 days	27/09/18 11:12 AM	4/10/18 11:12 AM	25
27		Documentación de la solicitud	5.714 days	4/10/18 11:12 AM	11/10/18 11:12 AM	26
28		<b>FASE 5. PRUEBAS DE LA SOLUCION</b>	<b>22.857 d...</b>	<b>11/10/18 11:12 AM</b>	<b>8/11/18 11:12 AM</b>	
29		Análisis de casos de uso y Manual d...	11.429 d...	11/10/18 11:12 AM	25/10/18 11:12 AM	27
30		Diseño y Ejecución del plan pruebas	11.429 d...	25/10/18 11:12 AM	8/11/18 11:12 AM	29
31		<b>FASE 6- IMPLEMENTACION</b>	<b>28.571 d...</b>	<b>8/11/18 11:12 AM</b>	<b>13/12/18 11:12 AM</b>	
32		Configuración de hw y sw	3.429 days	8/11/18 11:12 AM	13/11/18 11:12 AM	30
33		Ejecución del plan de integración en...	3.429 days	13/11/18 11:12 AM	16/11/18 11:12 AM	32
34		Instalación de la solución	3.429 days	16/11/18 11:12 AM	21/11/18 11:12 AM	33
35		Aplicación de pruebas funcionales (...)	5.714 days	21/11/18 11:12 AM	28/11/18 11:12 AM	34




jun 18					2 jul 18					9 jul 18					16 jul 18					23 jul 18					30 jul 18					6 ago 18					13 ago 18					20 ago 18					27 ago 18																							
M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D

**m Manzanero**

**Eric Ysmael Cocom Manzanero**

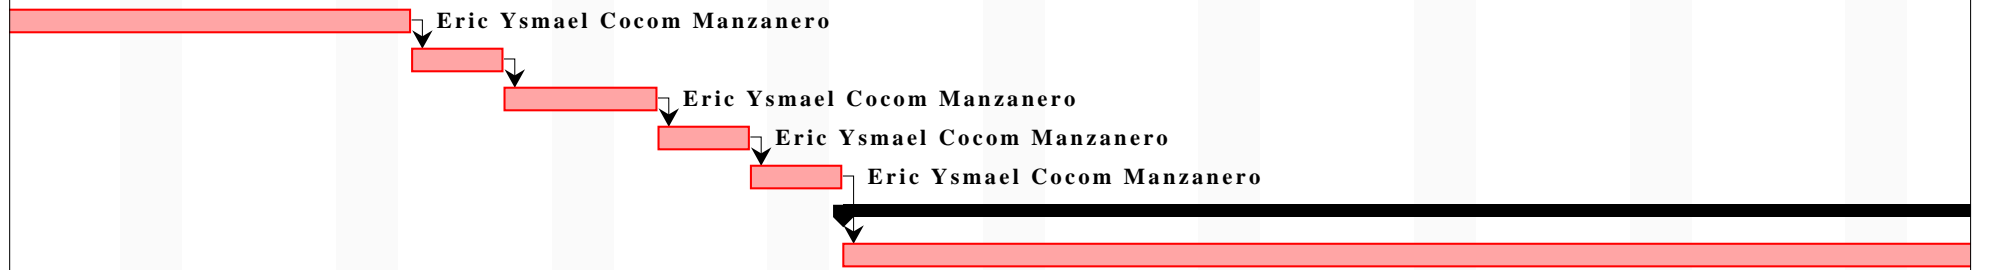


ago 18				3 sep 18				10 sep 18				17 sep 18				24 sep 18				1 oct 18				8 oct 18				15 oct 18				22 oct 18				29 oct																								
M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D

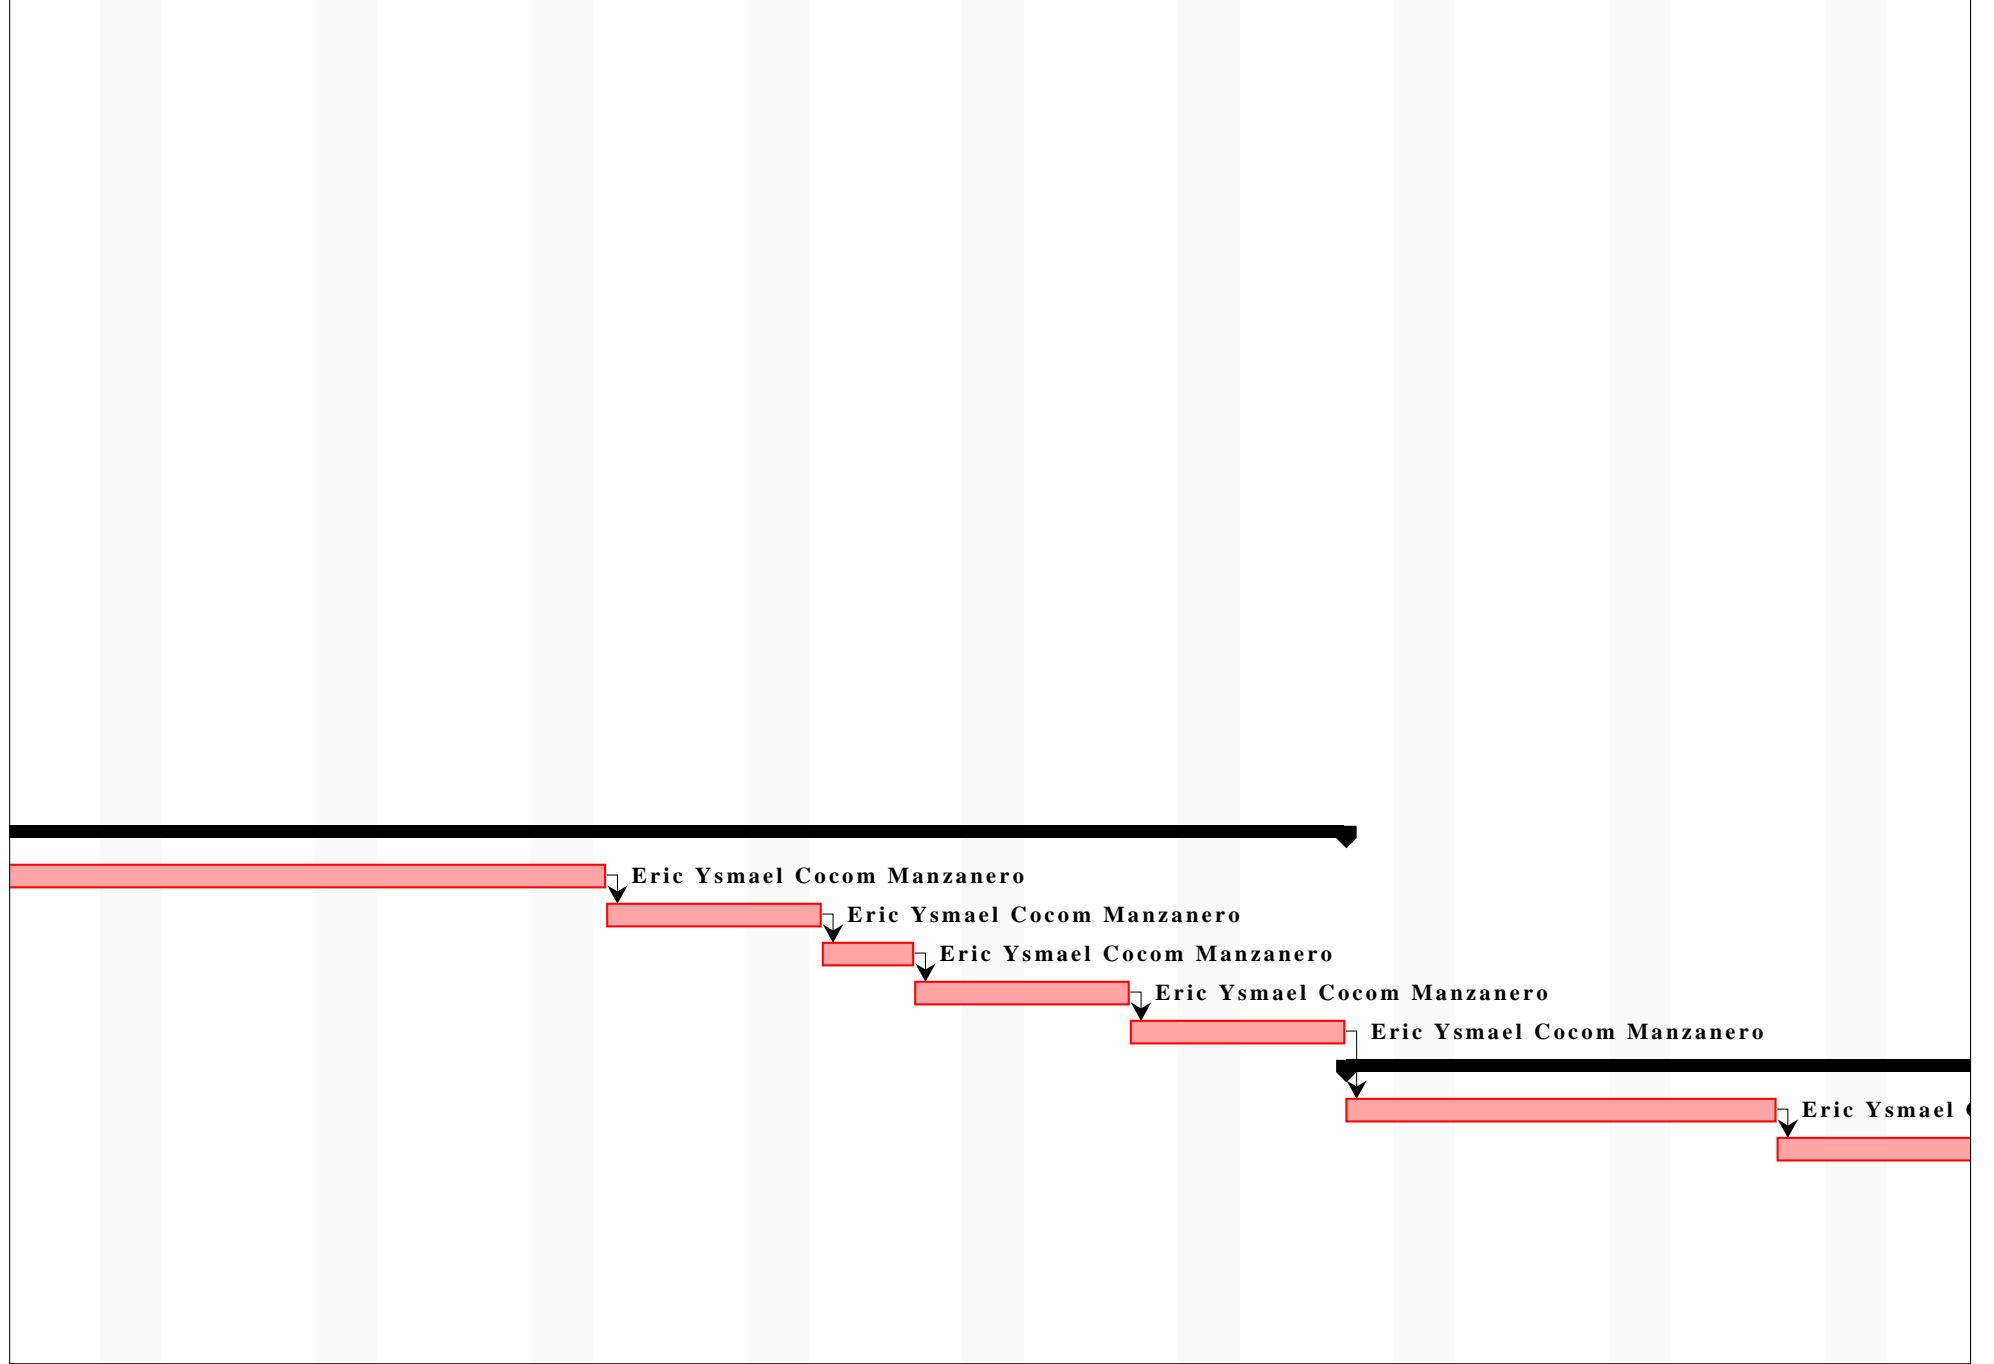


18	5 nov 18	12 nov 18	19 nov 18	26 nov 18	3 dic 18	10 dic 18	17 dic 18	24 dic 18	31 dic 18
J   V   S   D	L   M   M   J   V   S   D	L   M   M   J   V   S   D	L   M   M   J   V   S   D	L   M   M   J   V   S   D	L   M   M   J   V   S   D	L   M   M   J   V   S   D	L   M   M   J   V   S   D	L   M   M   J   V   S   D	L   M   M   J   V   S   D

**Cocom Manzanero**



8				7 ene 19					
V	S	D	L	M	M	J	V	S	D

		Nombre	Duracion	Inicio	Terminado	Predecesores
36		Capacitación tecnica	3.429 days	28/11/18 11:12 AM	3/12/18 11:12 AM	35
37		Capacitación a usuario	3.429 days	3/12/18 11:12 AM	6/12/18 11:12 AM	36
38		Seguimiento	5.714 days	6/12/18 11:12 AM	13/12/18 11:12 AM	37
39		<b>FASE 7. CIERRE DE PROYECTO</b>	<b>1.143 d...</b>	<b>13/12/18 11:12 AM</b>	<b>14/12/18 11:12 AM</b>	
40		Acta de cierre de proyecto	1.143 days	13/12/18 11:12 AM	14/12/18 11:12 AM	38
41		Carta de aceptación	1.143 da...	13/12/18 11:12 AM	14/12/18 11:12 AM	38

Nombres del Recurso	7 may 18			14 may 18			21 may 18			28 may 18			4 jun 18			11 jun 18			18 jun 18			25													
	V	S	D	L	M	J	V	S	D	L	M	J	V	S	D	L	M	J	V	S	D	L	M	J	V	S	D	L	M	J	V	S	D	L	N
Eric Ysmael Cocom M...																																			
Eric Ysmael Cocom M...																																			
Maria del Carmen Esp...																																			
Edgar Gómez																																			
Edgar Gómez																																			





ago 18				3 sep 18				10 sep 18				17 sep 18				24 sep 18				1 oct 18				8 oct 18				15 oct 18				22 oct 18				29 oct																															
M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D							



8 7 ene 19

V S D L M M J V S D

**Manzanero**
